


HawaiiBusiness' *2018 Best Places to Work*



**Week of 7/14/19**

**Construction  
Management By:**

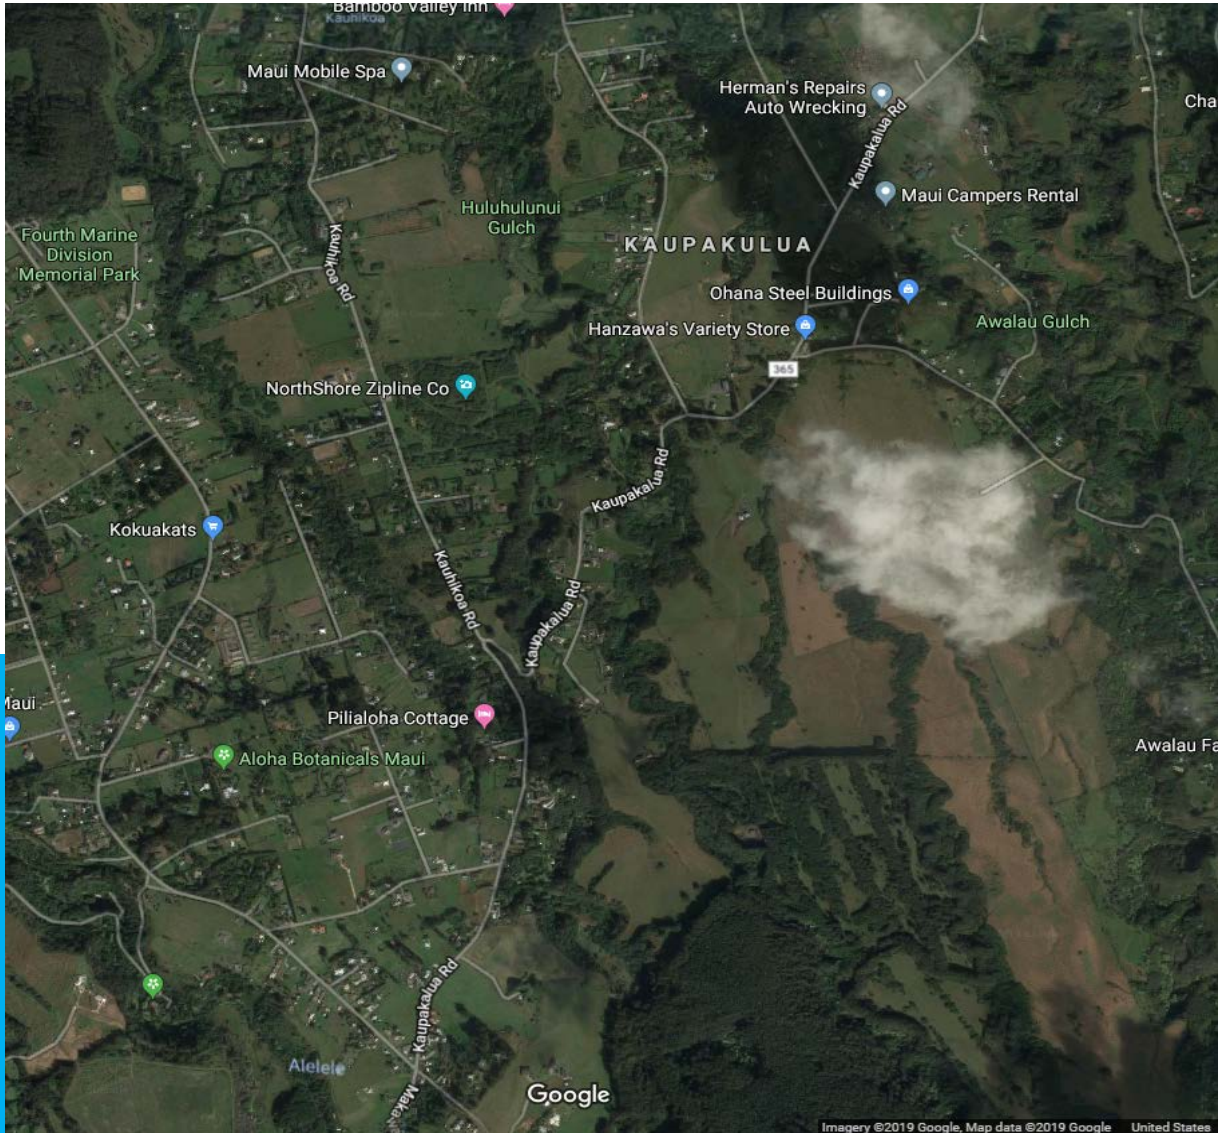

# Kaupakalua Rd Pavement Reconstruction

## Kokomo Rd to E. Kuiaha Rd

---

Island of Maui

Project Number: STP-0365(010)

### Project Scope:

This project involves the removal of existing pavement down to the gravel subbase within the road right-of-way, installation of a new asphalt concrete pavement section with reinforcing geogrid, new rigid pavement (Portland Cement Concrete) section for a small portion of the roadway, installation of new pavement striping and pavement markers, adjusting manhole and valve frames and covers where needed, removal/replacement of dented guardrails, removing/replacing signage & posts, and other incidental items.

### When:

Notice to Proceed: February 11, 2019

Contract Working Days: 287

Anticipated Completion Date: April 7, 2020 // Revised Completion Date: April 13, 2020

### Roads Involved:

Kaupakalua Rd from Kokomo Rd to E. Kuiaha Rd

### Contractor:

HI-Built, LLC  
72 Tings Dr  
Wailuku, HI 96793

### Contract Amount:

\$4,796,353.55

### Project Contact:

County of Maui, Department of Public Works  
Engineering Division  
(808) 270-7745

### Construction Update:

#### Work Completed Week of 7/7/19 – 7/13/19:

- No work scheduled to take place

#### Work Scheduled Week of 7/14/19 – 7/20/19:

- No work scheduled to take place
